FOR MYSORE STATE

27—95,006 31 10 50.

Dept (1953) Department.

Pam

MS SERIES.

G.O. NO.	511
Dated	3.2.53

[Despatch Abstract.]

Industries — Sericulture — yarn — silk filatures

Kollegal Erection of Atwood silk throwing Machinery and 20 Power looms. Electrical installation

Additional Expenditure — Sanction —

Department of Industries and Commerce.

From
Sri M.T.Raju, Bar-at-law, I.C.S.,
Director of Industries and Commerce,
'Mackays Gardens', Madras.6.

To
The Secretary to Government,
Development Department,
Fort St.George, Madras.9.

-x-x-x

Copy of Special Letter No.A.50/846 CE dated 20th June, 1952 from the Electrical Engineer (General) 35/38 , Thambu Chetty St., G.T.Madras - 1 to The Chief Engineer, P.W.D (Buildings), Chepauk, Madras.

Ref: Your Memo No.1282 Wks /52-53 - dated 22-5-1952 and this office No. 253 CE dated 29-5-52.

Sub: Industrees - Government Silk Filatures, Kollegal - Erection of Asiwoods Silk Twisting Machinery and 20 Power Looms - Electrical Instllation- Regarding.

33180

1. In G.O.No.3819 Development dated 19-7-1948 sanctioning the installation of a silk twisting plant at Kollegal, there is a provision of Rs.22,500/- under electrical installations. The expenditure on this work is chargeable to '85.A. Capital Outlay on Provincial Schemes of State Trading - C.Other Miscellaneous Schemes J.Government Silk Filatures, Kollegal'.

2. In G.O.No.4025 Development dated 8-9-1951 sanctioning installation of power-looms, there is a provisision of Rs.8,000/- only towards the electrical installation and this expenditure is stated to be chargeable to '43.Industries and Supplies - a. Industries - P.Goverhment Silk Filatures, Kollegal. 16900

3. In Development Department Memo No.45401 G/52-2 dated 13-5-1952 instructions have been issued for the completion of the work before the end of May 1952.

4. A combined estimate for the works sanctioned in the G.Os. referred to in para 1 and 2 above is under preparation and will be submitted separately for sanction under ' S.Remittance Payments on account of Civil Industries Department including centage at 15 ½ %. In view of the urgency expressed by the Director of Industries, the expenditure is proposed to be debited to that department for final adjustment to the final heads of account referred to in the G.Os. It is also taken for granted that necessary funds are reserved by the Director of Industries to meet the debit to be ultimately raised by this division.

5. As indicated in this office No.253 CE dated 29-5-1952 tenders were called for by this division for the portion of work to be completed by this division. Seven tenders were received for the work and they are all submitted herewith along with a detailed comparative statement. The earnest money deposit chalans are retained in this office. It will be seen from the comparative statement that the tender of Messrs Durai Bros., for Rs.15,52[illegible]/- is the lowest. This firm was recently enlisted as contractors in this division and they are now entrusted with a work costing about Rs.1,000/- in the College of Indian Medicine, Madras. The rates quoted by them are reasonable and as they appear to be professional well equipped their tender for this work which happens to be the lowest is recommended for favour of your acceptance.

6. Regarding the portion of the work to be executed by the Superintending Engineer, Pykara Electricity System viz., Provision of H.T.Supply, an estimate for Rs.29,640/- was received from the Divisional Engineer, Commercial, Coimbator It will be seen from his letter No.DCE/D1/7664/52 dated 10-6-1952(copy enclosed that the transformers are not available with him. I have written a D.O to the Superintendent Engineer, Pykara System (copy enclosed) suggesting the exclusion certain items from the estimate and his reply is awaited.

7. Taking matters as they stand for the present, the rough cost of the scheme will be as follows:-

Wiring etc., to be done by this division		Rs.16,400
H.T.Service connection by the Electricity Department.		29,640
Masonary works to be attended to by the Executive Engineer, Salem Division.		500
	Total.	46,540/-
Works		46,540-
Centage at 15 ½ %		7,214/-
		53,754 or Rs.53,800 roughly.

p.t.o.

As the provision in the scheme estimates as detailed in paras 1 & 2 is only Rs.30,500 there will be an excess of Rs.23,300/- requiring the sanction of Government if this excess cannot be met with from the 4.75 lakhs of the total non-recurring expenditure sanctioned in the G.Os. I am sending a copy of this letter to the Sericultural Expert, Kollegal for examining this position.

8. I request the favour of your early instructions and orders on the tenders submitted. In view of the commitments already made by the Industries Department and the urgency of work stressed by them the tenders may kindly be accepted ~~xxxx~~ early and orders issued to proceed with the work.

(True Copy)

r.n. 14.7.

5

SPECIAL.

PUBLIC WORKS DEPARTMENT

From

P.S. Venkataraama Ayyar, B.E., I.S.E.,
Chief Engineer, P.W.D. (Buildings),
Chepauk, Madras-5.

To

The Secretary to Government,
Development Department,
Fort St.George,
MADRAS.

Letter No.1282 Wks/52-8 dated 31-7-52.

Sir,

Subject: Government - Silk Filatures - Kollegal - Installation of silk twisting and weaving machinery - Electrical installation - regarding.

Ref:- Government Endt.No.80095 G/52-1 dated 21-7-52.

A copy of the instructions issued in my Memo.No.1282 Wks/52-5 dated 3-7-52 to the Electrical Engineer (General) on the subject is enclosed. Necessary action on the letter of the Director of Industries and Commerce No.4921 D-1/51 dated 12-7-52 may be taken by Government on receipt of the revised estimates called for in para (4) of my Memo. mentioned above. The Electrical Engineer (General) is being asked to expedite the revised estimate called for in the above Memo. and on its receipt it will be forwarded to Government.

for Chief Engineer, P.W.D.
(Buildings)

P.T.O.

Encl:- Copy of Chief Engineer's Memo.No.1282 Wks/52-5
dated 3-7-52.

wda/2-8.

Dev(Hq)2

Please see the Chief Engr's letter on p5 above received in reply to the Endt. on p1 above.

The receipt of the revised estimate may be awaited till 30.8.52.

11/8/52

11/8/52

11/9/52

IMMEDIATE

Office of the Chief Engineer, P.W.D. (General), Chepauk, Madras

Memorandum No.1282 Wks/52-2, Dated 3-7-1952.

Sub: Industries - Government -Silk Factories -Kollegal- Erection of (1) Atweeds silk twisting machinery (2) Twenty power looms - Electrical installation- Regarding.

Ref: From the Electrical Executive Engineer(General)No.895 CE dated 20.6.1952

It is seen from paras 1 and 2 of Electrical Executive Engineer's letter cited that the works (1) and (2) mentioned above have been sanctioned by Government in two separate G.Os and the expenditure is also debitable to different heads of account. The provision of electrical installations in connection with the works (1) and (2) above should therefore be treated as two separate works under the respective Government sanctions. The Electrical Engineer (General) has called for tenders for providing electrical installation in connection with (1) erection of Atweeds silk twisting machinery and (2) erection of 20 power looms together. If the work of providing electrical installation for items (1) and (2) are treated separately, the amount involved in each tender would be within Rs.10,000/- and the tenders will be within the Electrical Engineer(General)'s powers of acceptance. The tenders are therefore returned to the Electrical Engineer(General) and he is requested to split up the work of providing Electrical installation into two parts and deal with the tenders himself.

2. The rates of lowest tenderers M/s.Durai Bros. for items 2, 9, 10 and 17 of tender schedule are higher than the rates quoted by the next lowest tenderers M/s.Lakshmi Electric and Engineering Company. The Electrical Engineer(General) should examine if the rates of M/s. Durai Bros. for the above items could be get reduced by negotiations, before taking further action on the tenders.

3. The Electrical Engineer(General) should ascertain from the Director of Industries if the entire funds required for this work will be reserved to meet the expenditure this year.

4. It is seen from para 7 of Electrical Engineer (General)'s letter cited that the estimate cost of providing electrical installations in connection with the two works will exceed the Lump sum provision contained in the amounts sanctioned by Government for the respective schemes. The actual excess is not definitely known. The Electrical Engineer(General) has made certain suggestions to omit certain items to reduce the cost of H.T.service connection vide his letter No.4491 M d/17.6.52 to Superintending Engineer, Pykara Electricity System, and the actual excess in the estimates will be definitely known only after the estimate for H.T.service connection is finalised by the Electricity Department. The Electrical Engineer(General) should ascertain the correct excess in regard to the two works and find out from the Director of Industries and Commerce if the excess could be met within the amounts sanctioned by Govgrnm

P.T.O

4/

for the two schemes and submit a report in the matter to this office. He may also prepare the necessary estimates for providing electrical installations in connection with works (1) and (2) above based on the tender rates and submit the estimates together with the information mentioned above for obtaining the necessary revised administrative approval of Government, if necessary

2. In view of the urgency for the work, the Electrical Engineer(General) may accept the tenders in anticipation of sanction to estimates, in consultation with the Director of Industries and Commerce, and proceed with the work as expeditiously as possible.

T.S.VENKATARAMA AYYAR,

Chief Engineer(Buildings)/PWD.

To The Electrical Engineer(General).Madras.

Encl: 7 tenders
1 Comp.statement.

~~Forwarded/by order~~
(True copy)

Senior Superintendent.

ana/3.7.

9/

SPECIAL.

PUBLIC WORKS DEPARTMENT.

From

Sri T.S.Venkatarama Ayyar, B.E.,I.S.E.,
Chief Engineer,PWD (Buildings.),
Chepauk, Madras.5.

To

The Secretary to Government,
Public Works Department,
Fort St.George,
Madras.9.

Letter No.1282 Wks/52-11 dated 4-9-1952.

Sir,

INDUSTRIES - Government Silk Filatures, Kollegal - Erection of Atwood Silk Twisting Machinery and 20 Power looms - H.T.supply - Purchase of transfers - Regarding -

-- -- -- --

(B)

Government in Memorandum No.45,401 G/52-2 dated 13th May 1952 have ordered that the work of Electrical Installation in connection with the schemes for establishing the silk twisting section and 20 power looms at Government Silk Filatures, Kollegal should be given highest priority, and all steps taken to get the work completed expeditiously. I invite the attention of Government to my letter No. 1282 Wks/52-8 dated 31-7-1952 to Secretary to Government, Development Department (Copy enclosed) wherein I have already reported that the Electrical Engineer (General) has been instructed to carry on with the internal wiring as expeditiously as possible in anticipation of revised administrative approval of Government to the estimate for the work.

2. The Electrical Engineer (General) has now reported that he has since discussed the question of H.T.Service connections to Government Silk Filatures, Kollegal with the Chief Operation Engineer (South) and the latter has requested this Department to place orders for the transformers required for the works, and arrange them to be delivered to the Electricity Department at Coimbatore, who will carry out the work relating to H.T. Service connection and debit the cost to this Department against the estimate for the work. The Executive Engineer, Operating system obtained quotations for the transformers from the leading firms in the line and based on the quotations the Chief Operation Engineer (South) has recommended that orders may be placed for 4 Numbers single phase, 75 KVA, 13.2 KV Transformers on Messrs. Radio and Electricals Ltd., at a cost of Rs.4315/- each F.O.R.Coimbatore.

3. The different firms have quoted for different makes and the transformer selected is of a non-standard nature and Messrs. Radio and Electricals Ltd.,Madras are the only firm who have quoted for execution in a short time and their price is reasonable compared with the prices for other makes quoted by the other firms. The equipment proposed is of a "propriety character and competition is not considered necessary". The quotation of Messrs. Radio and Electricals Ltd. for the supply of the above transformers has therefore been treated as a single tender within the meaning of paragraph 11 of the instructions under Rule III of Article 125 of Madras Financial Code Volume I and has been accepted by me in view of the urgency of the work expressed in the Government Memorandum cited above. Necessary orders on the firm for supply of equipment has also been placed.

4. The detailed estimate for the work including provision ~~of~~ for the transformers and H.T.service connection etc., is awaited from the Electrical Engineer (General) and on receipt

on receipt it will be sent to Government for administrative approval. I request that my action in having treated the quotations of Messrs. Radio and Electricals Ltd., as a single tender under the above Code para and accepted the quotations and placed orders with the above firm for the supply of 4 Transformers at Rs.4315/- each F.O.R., Coimbatore, pending revised Administrative approval to the estimate for the work, may be ratified.

T.S.Venkatarama Ayyar,

for Chief Engineer, P.W.D.(Buildings.)

Chief Engineer's letter No.1282 Wks/52-8 dated 31-7-1952 with enclosures.

Endorsement No.1282 Wks/52-12 dated 4-9-1952.

Copy to:the Secretary to Government, Development Department in continuation of Chief Engineer's letter No. 1282 Wks/52-8 dated 31-7-1952.

for Chief Engineer, PWD (Buildings)

To

The Secretary to Government, Development Department.

Copy to: The Electrical Engineer (General) in continuation of this Office Endorsement No.1282 Wks/52-9 dated 31-7-1952.

vts.4-9.

Dept Deptt

Copy of this letter from the C.E. P.W.D (Buildings) may be alone addressed to the Govt. in P.W.D Deptt. may be perused. P.W.D will no doubt take necessary action and it is not clear. No action seems therefore called for in this deptt. The C.E.'s further report promised at para alone may be awaited till 20.9.52

11/9/52

Confdl

I think the C.E should be cautioned about this lapse in the dealings with the firm

P.W.

12-9-52

SPECIAL.

PUBLIC WORKS DEPARTMENT.

From

Sri T.S.Venkataraman Ayyar, B.E.,I.S.E.,
Chief Engineer,PWD (Buildings.),
Chepauk, Madras.5.

To

The Secretary to Government,
Public Works Department,
Fort St.George,
Madras.9.

DEPUTY SECRETARY TO GOVT. 74964 SEP 1952 PUBLIC WORKS DEPARTMENT

Sir, Letter No.1282 Wks/52-11 dated 4-9-1952.

INDUSTRIES - Government Silk Filatures, Kollegal - Erection of Atwood Silk Twisting Machinery and 20 Power looms - H.T.supply - Purchase of transformers - Regarding -

-- -- -- --

Government in Memorandum No.45,401 G/52-2 dated 13th May 1952 have ordered that the work of Electrical Installation in connection with the schemes for establishing the silk twisting section and 20 power looms at Government Silk Filatures, Kollegal should be given highest priority, and all steps taken to get the work completed expeditiously. I invite the attention of Government to my letter No. 1282 Wks/52-8 dated 31-7-1952 to Secretary to Government, Development Department (Copy enclosed) wherein I have already reported that the Electrical Engineer (General) has been instructed to carry on with the internal wiring as expeditiously as possible in anticipation of revised administrative approval of Government to the estimate for the work.

2. The Electrical Engineer (General) has now reported that he has since discussed the question of H.T.Service connections to Government Silk Filatures, Kollegal with the Chief Operation Engineer (South) and the latter has requested this Department to place orders for the transformers required for the works, and arrange them to be delivered to the Electricity Department at Coimbatore, who will carry out the work relating to H.T. Service connection and debit the cost to this Department against the estimate for the work. The Executive Engineer, Operating system obtained quotations for the transformers from the leading firms in the line and based on the quotations the Chief Operation Engineer (South) has recommended that orders may be placed for 4 Numbers single phase, 75 KVA, 13.2 KV Transformers on Messrs. Radio and Electricals Ltd., at a cost of Rs.4315/- each F.O.R.Coimbatore.

3. The different firms have quoted for different makes and the transformer selected is of a non-standard nature and Messrs. Radio and Electricals Ltd.,Madras are the only firm who have quoted for execution in a short time and their price is reasonable compared with the prices for other makes quoted by the other firms. The equipment proposed is of a "propriety character and competition is not considered necessary". The quotation of Messrs. Radio and Electricals Ltd. for the supply of the above transformers has therefore been treated as a single tender within the meaning of paragraph 11 of the instructions under Rule III of Article 125 of Madras Financial Code Volume I and has been accepted by me in view of the urgency of the work expressed in the Government Memorandum cited above. Necessary orders on the firm for supply of equipment has also been placed.

4. The detailed estimate for the work including provision of for the transformers and H.T.service connection etc., is awaited from the Electrical Engineer (General) and on receipt

12

-2-

on receipt it will be sent to Government for administrative approval. I request that my action in having treated the quotations of Messrs. Radio and Electricals Ltd., as a single tender under the above Code para and accepted the quotations and placed orders with the above firm for the supply of 4 Transformers at Rs.4315/- each F.O.R., Coimbatore, pending revised Administrative approval to the estimate for the work, may be ratified.

R. Lakshmanan 4/9/52

for Chief Engineer, P.W.D.(Buildings.)

Encl: Chief Engineer's letter No.1282 Wks/52-8 dated 31-7-1952-with enclosures.

vts.4-9.

P.W.D (C)

Devt Deptt U.O for necessary action (The reference relates to a Commercial deptt and the expre. is debitable to the departmental head. Necessary Centage charge are also to be recovered for the execution of the work by the P.W.D)

Grdhs. Sanction may be issued in Devt

13.9.52

13.9.52

Dc

104727

PWD No. 7496 4/52

13.9.52

UNDER SECRETARY
15 SEP 1952
DEVELOPMENT DEPARTMENT

T 3. 13

Copy of letter No.1282 Wks/52-8 dated 31-7-1952, from the Chief Engineer,PWD (Buildings), Madras.5., to The Secretary to Government,Development Department Madras.9.

Government Silk Filatures - Kollegal - Installation of Silk twisting and weaving Machinery - Electrical Installation - regarding -

Ref: Government Endorsement No.30095 G/52-1 dated 21-7-1952.

A copy of the instructions issued in my Memorandum No.1282 Wks/52-5 dated 3-7-1952 to the Electrical Engineer (General) on the subject is enclosed. Necessary action on the letter of the Director of Industries and Commerce No.4921 D-1/51 dated 12-7-52 may be taken by Government on receipt of the revised estimates called for in para (4) of my Memorandum mentioned above. The Electrical Engineer (General is being asked to expedite the revised estimate called for in the above Memorandum and on its receipt it will be forwarded to Government.

T.S.Venkataraama Ayyar,
Chief Engineer,PWD (Buildings)

Encl: Copy of Chief Engineer's Memorandum No.1282 Wks/52-5 dated 3-7-1952.

11

Copy of Memorandum No.1282 Wks/52-5 dated 3-7-1952 from the Chief Engineer,PWD (Buildings.), Chepauk, Madras.5., to the Electrical Engineer (General), Madras.

Industries - Government - Silk Filatures - Kollegal Erection of (1)Atwoods silk twisting machinery (2) twenty power looms - Electrical Installation - regarding -

Ref: From the Electrical Engineer (General) No.895 CE dated 20-6-1952.

It is seen from paras 1 and 2 of Electrical Engineer (General)'s letter cited that the works (1) and (2) mentioned above have been sanctioned by Government in two separate G.Os. and the expenditure is also debited to different heads of account. The provision of electrical installations in connection with the works (1) and (2) above should therefore be treated as two separate works under the respective Government sanctions. The Electrical Engineer (General) has called for tenders for providing electrical installation in connection with (1) Erection of Atwoods silk twisting machinery and (2) erection of 20 power looms together. If the work of providing electrical installation for items (1) and (2) are treated separately, the amount involved in each tender would be within Rs.10,000/- and the tenders will be within Electrical Engineer (General)'s powers of acceptance. The tenders are therefore returned to the Electrical Engineer (General) and he is requested to split up the work of providing Electrical Installation into two parts and deal with the tenders himself.

2. The rates of lowest tenderers Messrs. Durai Bros for items 2,9,10 and 17 of tender shhedule are higher than the rates quoted by the next lowest tenderers Messrs. Lakshmi Electrical and Engineering Co. The Electrical Engineer (General) should examine if the rates of Messrs.Durai Bros for the above items could be got reduced by negotiations, before taking further action on the tenders.

3. The Electrical Engineer (General) should ascertain from the Director of Industries if the entire funds required for

14

for this work will be reserved to meet the expenditure this year.

4. It is seen from para 7 of Electrical Engineer (Genl.)'s letter cited that the estimate cost of providing electrical installations in connection with the two works will exceed the L.S. Provisions contained in the amounts sanctioned by Government for the respective schemes. The actual excess is not definitely known, The Electrical Engineer (General) has made certain suggestions to omit certain items to reduce the cost of H.T. service connection vide his letter No.4491 M dated 17-6-1952 to Superintending Engineer, Pykara Electricity System, and the actual excess in the estimates will be definitely known only after the estimate for H.T. service connection is finalised by the Electricity Department. The Electrical Engineer (General) should ascertain the correct excess in regard to the two works and find out from the Director of Industries and Commerce if the excess could be met within the amounts sanctioned by Government for the two schemes and submit a report in the matter to this office. He may also prepare the necessary estimates for providing electrical Installations in connection with works (1) and (2) above based on the tender rates and submit the estimates together with the information mentioned above for obtaining the necessary revised administrative approval of Government if necessary.

5. In view of the urgency for the work, the Electrical Engineer (General) may accept the tenders in anticipation of sanction to estimates, in consultation with the Director of Industries and Commerce and proceed with the work as expeditiously as possible.

T.S.Venkatarama Ayyar,
Chief Engineer, PWD (Buildings.)

True Copy

Senior Superintendent.

vts.4-9.

VS/4/9

P.W.D (C) 11

"The copy of C.E's. letter on pp 9-10 ante and the notes of Deut thereon may be perused.

2. The orgl letter of the C.E received in this Deptt has been transferred to Deut Deptt for orders and action with P.W.D Secy. No. 74964/1521 dt 13.9.52

3. The file may be returned to Deut Deptt.

15/9/52

17.9.52. Dy.

Secy 106391

15.9.52

P.W.D No. 77510e/52-1

17-9-52

Dy (C) Deptt

UNDER SECRETARY 18 SEP 1952 DEVELOPMENT DEPARTMENT

W/R ref to A. on p 10 above, a draft Memo. to C.E.(P.W.D.) is submitted. Finance may see the case before issue.

24.9.52

24/9/52

P.W.D

Fin.

Dy No. 80095/52-3

25-9-52

ADL. DEPUTY SECRETARY TO GOVERNMENT 25 SEP 1952 PUBLIC WORKS DEPARTMENT

P.W.D (C)

The draft memo below may be perused and the file passed on to Finance

P.W.D. No. No. 80537/1521

X.52

1/X/52

1.10.52

1.10.52 Fin

ADDITIONAL DEPUTY SECRETARY TO GOVERNMENT 3 OCT 1952 FINANCE DEPARTMENT

16

The draft memo. below may be accepted.

Dev (G II)

K.S.

The draft Memo below may have issue.

Dev 114910 etc
13-10-52

UNDER SECRETARY
13 OCT 1952
DEVELOPMENT DEPARTMENT

Issued as Memo No. 80095 Gf/52-4 dy 16.10.52

D.C. Box 74

80237

Dev (G) Dept 17

Confidential

Memo No 80095 G/52-4 dt 16.10.52

Sub: Industries G.S.F. K. Nagar – Erection of Atwood Sdh Twisting Machinery and 20 power looms – Electrical installation

Ref: Form No C.E. P.W.D. (Buildings) No. 1282 WKs/ dt 4.9.52

In the circumstances stated by the C.E. P.W.D (Buildings) in his letter cited, the Govt ratify his action in having invited the quotation of M/s Radio and Electricals Ltd. Madras for the supply of four transformers as a single tender within the meaning of paragraph 11 of the

P.T.O

18.

instructions under Rule III of Article 125 of the Madras Financial Code Vol. I. He is however informed that the affairs of M/s. Radio and Electricals Ltd., Madras are under enquiry and he should therefore be cautious in his dealings with this firm.

24.9.52 24/9/52

D.S.E.E. 30.9.52

To The C.E. P.W.D (Buildings)

Copy to D.I.G.

Department of Industries and Commerce.

From
Sri M.T. Raju, Bar-at-law, I.C.S.,
Director of Industries and Commerce,
'Mackays Gardens', Madras.6.

To
The Secretary to Government,
Development Department,
Fort St.George, Madras.9.

No.4927 D 1/51 dated 8-11-1952.

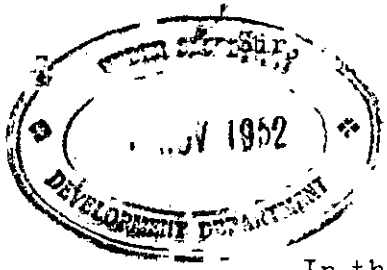

Sub: Industries - Government Silk Filatures, Kollegal - erection of Atwoods' Silk Twisting machinery and power looms - electricial installations - regarding.

Ref: This office letter No.4927 D 1/51 dated 12-7-1952.

In this office letter cited above, I had requested for sanction of an additional expenditure of Rs.23,300/- as the total amount of Rs.30,500 sanctioned in G.O.M.S.No.2024 Development dated 9-5-52 and G.O.M.S.No.4025 Development dated 8-9-1951 was found to be insufficient for completion of the electrical installations work connected with silk twisting plant and power looms at the Government Silk Filatures, Kollegal. The Electrical Engineer (General), Madras has since furnished a revised estimate (enclosed) for Rs.33,100/- in respect of the silk twisting section and for Rs.16,900/- in respect of the power loom weaving section. It is now seen that the total expenditure amounts to Rs. 50,000/- as against ~~from those estimates~~ the sum of Rs.35,500/- already sanctioned in the G.O's cited. The additional amount involved would be therefore Rs.19,500/-. In the circumstances I request that Government may be pleased to accord administrative approval of the plans and estimates for the work connected with the electrical installation of the silktwisting and power loom weaving sections and sanction an expenditure of Rs.19,500/- in addition to the amounts sanctioned in the G.O's referred to above, for the electrical installations, in lieu of the amount of Rs.23,300/- asked for in this office letter cited above.

p.n. 8.11.

For Director of Industries and Commerce.

Remarks under issue
11.12.52
Deptt Deptt

Endt No 80095 Q/52-7 dt. 24-11-52

Referred to Exec C.E. PWD (Poindings)
for very urgent remarks. His attention
is invited to his letter
No 1282 WKS/52-8 dt 31-7-52.

22/11/52

Spoken
to the C.E. PWD
Poindings. Work
copy 20/19 alig and A/ment 20 the
with plans and
estimate in original
may be returned with
reply.
R.D. 26-12-52

21

PUBLIC WORKS DEPARTMENT.

From
Sri T.S.Venkatarama Ayyar,
B.E.,I.S.E.,
Chief Engineer,PWD (Buildings)
Chepauk, Madras.5.

To
The Secretary to Government,
Development Department.

Letter No. 1282 Wks/52-21 dated 6-11-52.

127639

Sir,

Sub: Industries - Sericulture - Government Silk Filatures, Kollegal - Installation of Attwoods Silk Twisting Machinery and 20 power looms - Revised estimate -

Refce: Govt. memo No.80095 G/52-6 d/23-10-52. — R.F. ref. [illegible]

Revised estimates for each of the two works mentioned above viz., installation of Silk Twisting Machinery and -- installation of 20 power looms have been prepared by the Electrical Engineer (General) and sent to the Sericultural Expert for obtaining the coutersignature of the competent ~~Authority~~ Authority and the revised administrative approval of Government. The Sericultural Expert or the Director of Industries and Commerce may kindly be addressed by Government for the present stage of the revised estimates.

for Chief Engineer,P.W.D.(Bldgs.)

ska/7-11-52

Dev (G) Dept

T.M.

From H.S. Dev. Dept.

To Shri D.I.&C.

Sub: Industries. G.S.F. Kolleyal — Erection of Atwoods' Silk Twisting Machinery and power looms. Electrical installation.

Ref: Your letter No. 4927 D.I/57 dt 8.11.52

The revised estimate prepared by the Electrical Engineer (General) said to have been enclosed with your reference cited has not been received. Please send it immediately.

25

Industries & Commerce Department.

--

From
The Director of Industries & Commerce,
Mackey's Garden, Madras-6.

To
The Secretary to Government,
Development Department,
Madras.

No.4927 D.1/51 dated 18-11-1952.



1316/47 Glr 18.11.52 Filahme

Sir,

Sub: Industries - Sericultural Government Silk ~~Factory~~, Kollegal erection of silk twisting plant and power looms - Electrification.

Ref: This office letter No.4927 D.1/51 dated 8-11-52.

The plans and estimates referred to in this office letter cited above are herewith submitted.

Encl:
1. Estimate for Rs.33100/- (two sheets)
2. Revised estimate for Rs.23,800/-(1 sheet)
3. Blue print No.E.E.119/CBE/5253
4. Blue print No.E.E.121/CBE/52-53
5. Plan (on white paper) No.122/CBE/52-53
6. Estimate for Rs.16,900/- (2 sheets)
7. Blue Print No.122/CBE/52-53.

For Director of Industries & Commerce

KRV/18-11

Special:

PUBLIC WORKS DEPARTMENT,

From Sri T.S. Venkatarama Ayyar, B.E., M.I.E.(Ind.), I.S.E., Chief Engineer, P.W.D.(General and Buildings), Chepauk, Madras.

To

The Secretary to Government, Development Department. Madras.

LETTER No. 1282. Wks/52-22, dated 12-12-1952.

Sir,

Dis 142685 G/52 16.12.52



Sub:-Industries - Government Silk Filatures, Kollegal - Erection of Atwoods' Silk Twisting machinery and power looms - Electrical installations - regarding.

Ref:-Government endorsement No.80095.G/52-7, dated 24-11-1952.

The proposals of the Director of Industries and Commerce in his letter No.4927. D1/51 dated 8-11-1952 are based on the revised estimates, prepared by the Electrical Engineer, (General) adopting Tendered rates. The proposals of the Director may therefore be approved and orders issued accordingly.

2. The plans and estimates received with the Government endorsement are returned herewith.

for Chief Engineer, P.W.D.(Genl.&Bldgs),

Encl:
Plans and Estimates.
Gk.12/12/52.

29

Dev 7276 D1/53
20/1/53

Industries and Commerce Department.
***

From
The Director of Industries
and Commerce, Madras.6.

To
The Secretary to Government,
Development Department,
Fort St.George,Madras.

= = = =

Dev. (G) Deptt.

Sub:- Industries - Sericulture - Govt. Silk Filatures Kollegal - Erection of Atwood Silk Twisting machinery and 20 power looms - Electrical installations - Additional expenditure - Sanctione

Read:- G.O.Ms.No.2024, Dev. Dt. 9-5-52.
G.O.Ms.No.4025 Dev. dt. 8-9-51.

Read also :- From the D.I.& C. Letter No.4927/ DI/51, dated 12-7-1952, and 8-11-1952.
From the C.E.P.W.D.(General) Letter No.1282 Wks/52-22, dated 12-12-1952.

G.O.Ms.No. 511 Dev. dt. 3-12-1952

In the circumstances stated in his references cited and in partial modification of the orders issued in G.O.Ms.No.2024 Devt. dt. 9-5-52 sanction is accorded to an expenditure not exceeding Rs. 33,100/- (Rupees Thirty three thousand and one hundred only) towards electrical installation in connection with the establishment of the Silk Twisting Plant at the Govt. Silk Filatures, Kollegal.

The expenditure should be debited to "72 - Capital Outlay on Industrial Development - a. Investments in Govt. Commercial undertakings - G. Govt. Silk Filatures". The D.I.& C. should apply in time for additional appropriation of funds if necessary.

2. The Govt. also sanction an expenditure not exceeding Rs. 16,900/- (Rupees sixteen thousand and nine hundred only) towards electrical installations relating to looms, dye section etc. in lieu of the sum of Rs. 8,000/- (Rupees Eight thoundand only) sanctioned in G.O.Ms.No.4025 Development dated 8-9-51 in connection with the installation of 20 power looms at the Govt. Silk Filatures, Kollegal.

The expenditure should be debited to "43 - Industries and Supplies - a. Industries - P. Govt. Silk Filatures, Kollegal." The D.I.& C. should apply in time for additional appropriation of funds if necessary.

3. The plans and estimates for the work connected with the electrical installation of the Silk Twisting and Power Loom weaving sections are approved.

4. The action of the D.I.& C. in having requested the C.E. P.W.D. (General & Building) to proceed with the work in anticipation of provision of funds during the current year is also approved.

Para 3 or 1

Compld 4.2.53

To
The D.I.& C. along with plansand estimates.
The A.G. thro' Fin.
The CE. P.W.D (General & Building).

24.1.53.

Sec. 3
SF.

C. P. 304.—9,193 bks.—28111-47.

ORDER SECRET

OFFICE OF THE U.S. 17407

Date 14 FEB 1903 Hours Minutes 9 & c

ENVELOPE TO BE RETAINED

MESSAGE.

From C. E. (Bld.) | To A.S to Govt In Dept.

Subj. Education - Scientific Govt. civil Polytechnics - College erecting 7 Atwood civil Turning machinery & do panchaama festival installations - Additional expenditure - Sanctioned.

Ref: Govt. no. 511 d 3.2.03 (E)

The Copy of the above Govt received in this office is not endorsed with the State Emblem Please state whether the action may be taken on it.

Why

Please write on both sides.

33

17593

Office of the Chief Engineer, P.W.D., (General), Chepauk, Madras.

POST COPY OF THE TELEPHONIC MESSAGE No. 1282 Wks/52-23, Dt.14-2-53

From - The Deputy Chief Engineer, P.W.D., (Buildings).
Chepauk, MADRAS.

To - The Assistant Secretary to Government, Development Department, Fort St. George.

***

Sub: Industries - Sericulture - Government Silk Filatures, Kollegal - Erection of Atwoods Silk Twisting Machinery and20 power looms Electrical Installations - Additional expenditure Sanctioned.

Ref: G.O. No. 511, dated 3-2-1953. -TP 31-3-53 (B)

-:-

The copy of the above G.O. received in this office is not embossed with the State Emblem. Please state whether action may be taken on it.

(TRUE COPY)

SENIOR SUPERINTENDENT.

vd 14.2.

14/2

DEV (G)

T.M. T.M. dated 29.2.53

20 20 CE (Bldgs)

Sub:- Industries - Sericulture - G.S.F. Kollegal -
Erection of Atwood Silk Twisting machinery
and 20 power looms. - Electrical installations
Additional expenditure. G.O. No. HS 511 Dated 3-2-53.

Ref:- (~~Your~~ T.M. No. 1282 WKS/52-23 dated 14-2-53.

You may take action on the copy of
G.O. No. 511 DEV dated 3.2.53 received by you.

18/3/53.

Ref. Plan Estt. Sec. 16

5/1/57 Dev (G)

With reference to under Secretary's query on p/ep it is submitted that sometimes embossed manifolding sheets are in short supply in office and the practice then appears to be to type the copy intended for the A to alone on embossed sheets. Attention in this connection is invited to a note at (V). The C.E. may be informed that action may be taken on the copy of the orders received by him. A draft T.N. is submitted for approval.

(V)

19/2/57

Now put up.

18/7/57

C.C.B does not comply with the requirements of Such forms Stores Dept. The embossed sheets (both which and manifolding sheets) have in Bulk already been distributed to all depots further words of February 1953. Consequently the use of these forms had to be restricted. C.C.B. has now supplies in Bulk the requirements of the depots & forms have been supplied to all depots

19/11/57

Copy 19/11/57

INDUSTRIES AND COMMERCE DEPARTMENT 26000

From
The Director of Industries
and Commerce, Madras.6

To
The Secretary to Government,
Development Department, Madras.9

No.4927-D1/51. dated 3-3-1953

Sub: Industries - Sericulture, Government Silk Filatures, Kollegal - erection of silk Twisting plant and power looms - electrification

Ref: This office letter No.4927.D1/51 dt. 18-11-52. pp 25 of (C)

G.O.Ms.No.511 Dev., dt. 3-2-53. - pp 31-32 of (C)

I request that the plans submitted to Government with this office letter first cited above may kindly be returned to me as the Electrical Engineer General has called for the same.

for Director of Industries and Commerce.

trs/ 3/3.

DEV(G)

Memo No. 26000 G/53-1 dated 7.3.53

sub:- Industries - sericulture - G S F Kollegal
Erection of Atwood silk Twisting machinery -
electrification.

Ref:- From the D DOC No. 4927 D1/51 dated 3.3.53

A copy of the letter cited is forwarded to the CE. PWD (Gdl & Bldgs). The CE is requested to forward to the Electrical Engineer (General) direct the plans and estimates sent with the post copy of telephonic message dated 20.2.53 under intimation to the D.DOC and to this Govt.

p1 cf —

Final Plan
10.3.53

p35 cf (c)

The CE PWD (Gdl & Bldgs) (with a copy of p1 cf)
Copy to the D.DOC
Copy to the Electrical Engineer (General)

7/3/53

12.3.

Rd. 25.3.53.

Note issue the papers may be called

4

with GO Ms No 511 dated 3.2.53

pp 31-34 of (c)

PUBLIC WORKS DEPARTMENT.

From Sri T.S. Venkatarama Ayyar, B.E., M.I.E.(Ind.), I.S.E., Chief Engineer, PWD. (General and Buildings) Chepauk, Madras.

To

The Secretary to Government, Development Department.



Letter No. 282 Wks/52-26. d/ 18-3-1953

Sir,

INDUSTRIES - Sericulture - Government Silk Filatures, Kollegal - Erection of Atwoods Silk Twisting Machinery - Electrification -

34910

P3 above — Ref: Government Memorandum No.26000 G/53-1 dated 7-3-53.

The plans and estimates relating to the work have since been sent to the Electrical Engineer (General) after according the necessary Technical sanction to the work.

R. Lakshmanan 20/3/53

for Chief Engineer, PWD General and Buildings.

Copy to: The Director of Industries and Commerce, Madras.

vts.20-3.

2 Encl 51 Dev (S)

b/

Submitted for perusal.
No further action is called for. The papers may be filed with GO No. 511 Dev dated 3.2.53 -(C)

27.3.53

27/3/53

C.No.80095 G/52.

Devt. Dept.

Sub:- Industries - Sericulture - Govt. Silk Filatures Kollegal - Erection of Atwood Silk Twisting machinery and 20 power looms - Electrical installations - Additional-expenditure - Sanction of - Requested.

Ref:- From the D.I.& C.Letter No.4927 DI/51-, Dev. dated 21-7-1952.
† [Issued as Endorsement No.80095 G/52-1, Dev. dated 21-7-1952.]
= From the C.E. P.W.D.(Bldgs.) letter No.1282 Wks./8, dated 31-7-1952.
— [Issued as Memorandum No.80095 G/52-4, Dev. dated 16-10-1952.]
@ From the D.I.& C. Letter No.4927 DI/51-, dt. 8-11-1952.
× [Issued as Endorsement No.80095 G/52-7, dated 24-11-52]
From the C.E. P.W.D.(General) Letter No.1282 WKS/52-22, dt. 12-12-1952.

In G.O.Ms.No.2024 Devt. dt. 9-5-52 the Govt. have, among others, sanctioned a non-recurring expenditure of Rs. 22,500/- towards electrical installation in connection with the erection of the Atwood Silk Twisting Plant at the Govt. Silk Filatures, Kollegal. The expenditure is debitable to "72. Capital outlay on Industrial Development - a Investments in Govt. Commercial undertakings-G. Govt. Silk Filatures.

In connection with the installation of 20 power looms at the Govt. Silk Filatures Kollegal, the Govt. have in G.O.Ms.No.4025, Devt. dt. 8-9-51, sanctioned, among others, an expenditure of Rs. 8,000/- towards electrical installations. The expenditure is debitable to "43- Industries and Supplies a - Industries.P. Govt. Silk Filatures, Kollegal."

2. Attention is invited to the correspondence on pp. 1, 5, 19 and 27 c.f. The D.I.& C. has reported that at the time when the schemes were formulated and Govt. sanction obtained, it was not expected that the cost of H.T. Service connection will have to be borne

in respect of the two schemes referred to in para 1 above. The estimates include centage charges at 15½ per cent. The revised estimates of expenditure on electrical installation for the Silk Twisting Section is estimated to cost Rs. 33,100/- and that of the power loom Rs. 16,900/- The revised estimates may be approved.

3. The D.I.& C. has reported that the sum of Rs. 25,000/- provided for in the budget estimates for 1952-53 for the purchase of a Humudifier in connection with the installlation of the Silk Twisting Plant will not be utilised during the current yea[illegible] the amount may be utilised for incuring the additional expenditure for electrical installations. As however the expenditure is debited to two separate heads of account, the D.I.& C. may be asked to apply in time for additional funds to meet the expenditure. ~~The D.I.& C. may be asked to apply in time for additional funds to meet the expenditure~~. The D.I.& C.'s action in having requested the Chief Engineer P.W.D. to go ahead was the work in anticipation of Govt. approval of the revised estimates may also be approved.

Subject to orders a draft order is submitted below for approval. P.W.D. and Finance may see for acceptance.

22/12/52 22/12/52

P.W.D./Fin.

29/12

P.W.D(C)

ADDITIONAL DEPUTY SECRETARY TO GOVERNMENT 99855 31 DEC 1952 FINANCE DEPARTMENT

110968 PUBLIC WORKS D[illegible]

The note of Dept left from p1 ante may be perused. The draft order below may be accepted and the file passed on to Finance

30/12/52 30/12/52 31.12.52 31.12.52

Order No 110968 C1/52

31.12.52

This E Section

30/12/52

Fin 31/12 A S [illegible]

Finance (Expl)

P. see the notes on p.p. 1-2 above.

2. The draft order below may be accepted. The excess over the original estimates sanctioned in the G.O.s at (M) and (R) amounts to Rs. 19,500. The reasons for the excess are given in para 2 on p.1 above.

Dev

Dev. (G) Dept.

Notes from p.1 above may be perused.

The file relates to the proposals of the D.I.&.C for the sanction of revised estimates of expenditure in respect of the following schemes.

(i) Electrical installation in connection with the erection of Atwood Silk Twisting Plant at the Govt. Silk Filatures, Kollegal.

(ii) Electrical installation in connection with the installation of 20 power looms at the Govt. Silk Filatures, Kollegal.

The excess expenditure over the original estimates amounts to Rs. 19,500. Finance Deptt. have accepted the proposals of the D.I.& C.

The draft order below maybe circulated M.(I.& I for approval.

24.1.53

28/1/53

UNDER SECRETARY 21 JAN 1953 DEVELOPMENT DEPARTMENT

DEPUTY SECRETARY TO GOVERNMENT 20 JAN 1953 DEVELOPMENT DEPARTMENT

SECRETARY TO GOVERNMENT 29 JAN 1953 DEVELOPMENT DEPARTMENT
